ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors
1		**21417 ODOT 210170 SR-58 Four Lane Resurfacing - Lorain County**	**79 days**	**Thu 4/22/21**	**Tue 8/10/21**	
2		Preconstruction Meeting	1 day	Thu 4/22/21	Thu 4/22/21	
3		MOT Setup - Signs + Barells	2 days	Mon 5/3/21	Tue 5/4/21	2
4		Staking/ Layout	2 days	Mon 5/3/21	Tue 5/4/21	3SS
5		Concrete Repairs - Ridge Replacement	6 days	Mon 5/17/21	Mon 5/24/21	4
6		Concrete - Curb and Sidewalk (Remove and Install)	12 days	Tue 5/25/21	Wed 6/9/21	5
7		Pavement Repairs - Asphalt	5 days	Mon 5/31/21	Fri 6/4/21	6SS+4 days
8		Pavement Planing	6 days	Mon 6/7/21	Mon 6/14/21	7
9		Workzone Marking	6 days	Mon 6/7/21	Mon 6/14/21	8SS
10		9.5 MM Placement	6 days	Tue 6/15/21	Tue 6/22/21	8
11		Workzone Markings	6 days	Tue 6/15/21	Tue 6/22/21	10SS
12		Adjustments	15 days	Wed 6/23/21	Tue 7/13/21	11
13		Guardrail Install	15 days	Wed 7/14/21	Tue 8/3/21	12
14		Install Berm	2 days	Wed 8/4/21	Thu 8/5/21	13
15		Final Pavement Markings	3 days	Fri 8/6/21	Tue 8/10/21	14

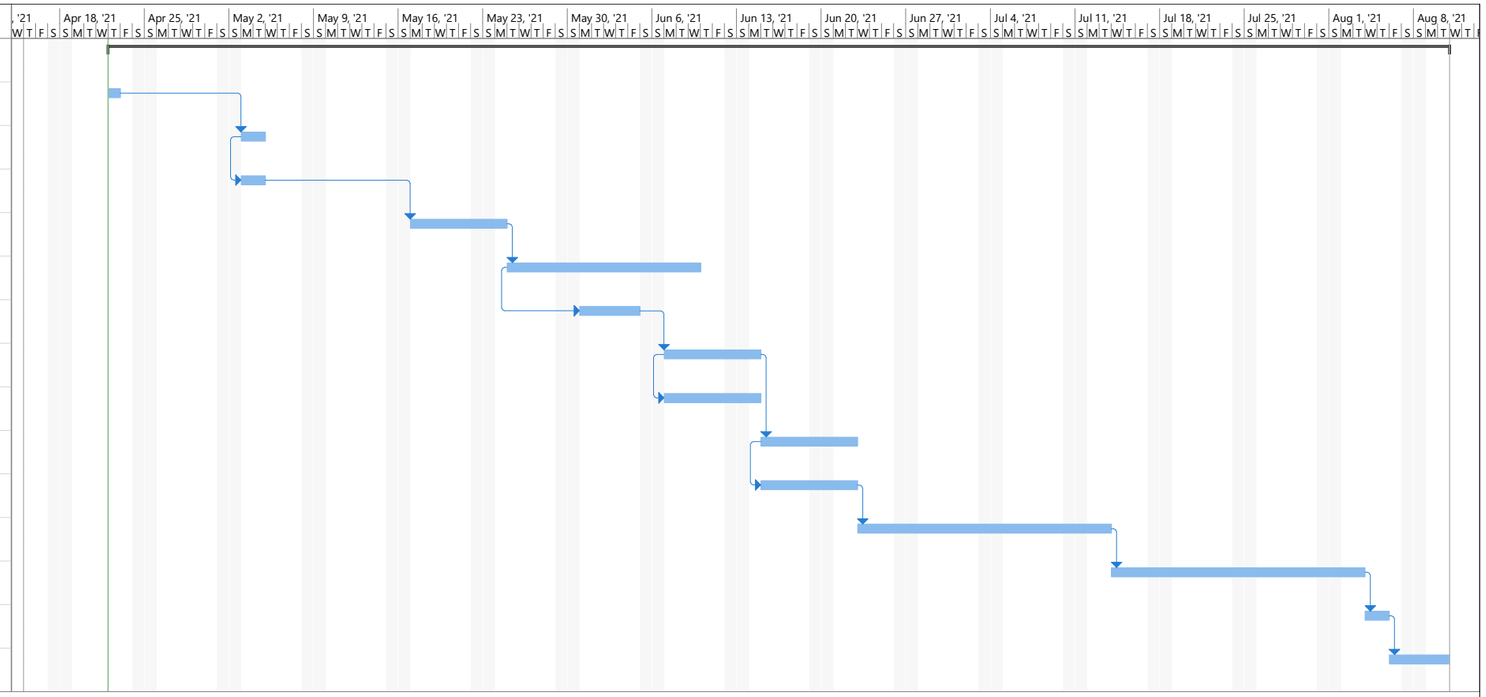

Project: 21417 ODOT 210170 S
Date: Thu 4/22/21

Task	Summary	Inactive Milestone	Duration-only	Start-only	External Milestone	Manual Progress
Split	Project Summary	Inactive Summary	Manual Summary Rollup	Finish-only	Deadline	
Milestone	Inactive Task	Manual Task	Manual Summary	External Tasks	Progress	
